Exhibit_____(AM-2)
Elm Road Generating Station Schedule

ID	Task Name	Start	Finish
1	**PSCW**	**Fri 2/1/02**	**Mon 11/10/03**
2	Submit Application	Fri 2/1/02	Fri 2/1/02
3	Completeness Review	Tue 9/3/02	Wed 10/2/02
4	CPCN Process	Thu 10/3/02	Mon 11/10/03
5	Order Issued	Mon 11/10/03	Mon 11/10/03
6	**DNR**	**Fri 10/26/01**	**Fri 2/13/04**
7	Submit Engineering Plan	Fri 10/26/01	Fri 10/26/01
8	List of Permits	Fri 10/26/01	Mon 11/26/01
9	Permit Applications Due	Tue 11/27/01	Mon 12/17/01
10	Permit Process	Tue 12/18/01	Fri 2/13/04
11	Site Preparation	Mon 2/2/04	Mon 3/1/04
12	Notice to Proceed	Mon 3/1/04	Mon 3/1/04
13	**Elm Road SCPC and IGCC**	**Fri 11/16/01**	**Sun 5/1/11**
14	**Engineering & Procurement**	Fri 11/16/01	Fri 4/29/11
15	**SCPC Project Construction**	**Tue 3/2/04**	**Fri 5/1/09**
16	Earthwork	Tue 3/2/04	Mon 2/28/05
17	Common Facilities	Tue 3/2/04	Fri 9/29/06
18	Railroad upgrades	Thu 4/1/04	Fri 1/19/07
19	Material Handling	Mon 5/3/04	Fri 10/31/08
20	**SCPC Unit 1**	**Thu 12/2/04**	**Thu 5/1/08**
21	SCPC1 Foundations	Thu 12/2/04	Mon 5/2/05
22	SCPC1 Structural Steel Erection	Tue 5/3/05	Fri 2/3/06
23	SCPC1 Boiler Erection	Wed 11/2/05	Mon 7/2/07
24	SCPC1 Turbine Installation	Mon 2/6/06	Fri 2/2/07
25	SCPC1 Startup and Testing	Thu 4/5/07	Thu 5/1/08
26	SCPC1 Commercial Operations Date	Thu 5/1/08	Thu 5/1/08
27	**SCPC Unit 2**	**Wed 12/7/05**	**Fri 5/1/09**
28	SCPC2 Foundations	Wed 12/7/05	Tue 5/9/06
29	SCPC2 Structural Steel Erection	Wed 5/10/06	Tue 2/6/07
30	SCPC2 Boiler Erection	Fri 11/3/06	Mon 6/30/08
31	SCPC2 Turbine Installation	Wed 7/4/07	Mon 6/30/08
32	SCPC2 Startup and Testing	Thu 4/3/08	Fri 5/1/09
33	SCPC2 Commercial Operations Date	Fri 5/1/09	Fri 5/1/09
34	**IGCC Project Construction**	**Thu 8/23/07**	**Sun 5/1/11**
35	IGCC Site Development and Demolition	Thu 8/23/07	Tue 6/17/08
36	IGCC Gasification Facility Erection	Thu 4/17/08	Wed 10/27/10
37	IGCC Combined Cycle Erection	Fri 7/18/08	Thu 8/26/10
38	IGCC Startup and Testing	Tue 11/24/09	Fri 4/29/11
39	IGCC Commercial Operations Date	Sun 5/1/11	Sun 5/1/11
40	**Transmission**	**Tue 11/11/03**	**Sun 5/1/11**
41	Phase I	Tue 11/11/03	Thu 10/11/07
42	Phase 2	Mon 8/25/08	Fri 5/1/09
43	Phase 3	Mon 5/4/09	Sun 5/1/11

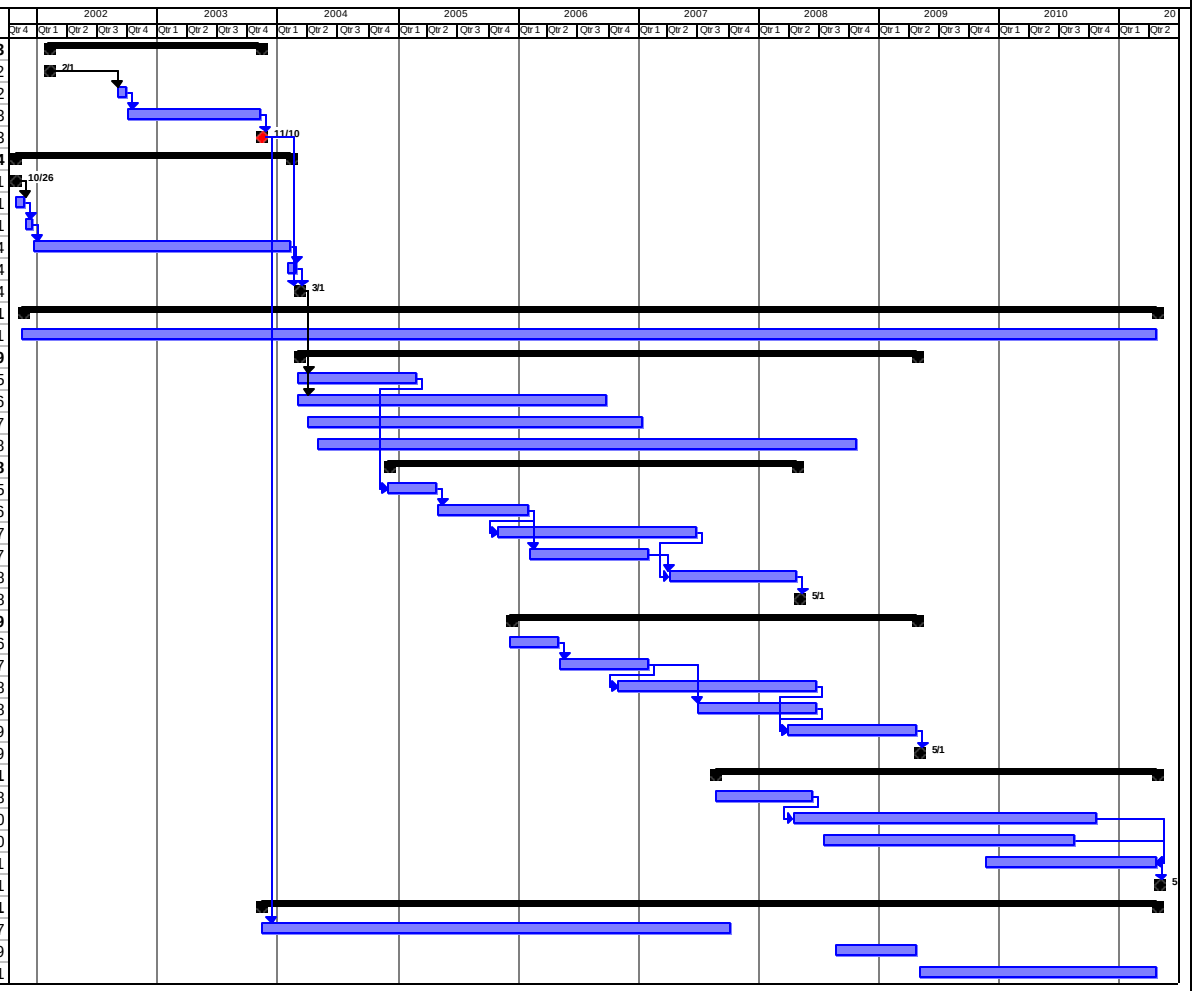

Project: OC CPCN Schedule 011116
Date: Thu 5/22/03

Task | Milestone | Rolled Up Task | Rolled Up Progress | External Tasks
Progress | Summary | Rolled Up Milestone | Split | Project Summary
